

**Canadian Natural Resources Limited
GENERAL PRESSURE VESSEL INFORMATION**

Job # 10.111579

District: Fort St. John BC.	Skid No.
Facility: Jedney Gas Plant	Location (LSD): a-62-E/94-G-8
Vessel Name Equipment Number: Condensate Storage Vessel	
Orientation: Horizontal	
Status: In Service	Regulatory Inspection

PRESSURE VESSEL NAMEPLATE DATA

"A" or "G" or "S" (Sask.) or BC Registration Number. A242824		CRN Number: F -7745.1	
Vessel serial number: 88-1032		Size: 60 in. x 16 ft.	
Shell thickness: 15.9mm		Shell material: SA 516-70N	
Head thickness: 15.4mm		Head material: SA 516-70N	
Tube wall thickness:		Tube material:	
Tube diameter:		Tube length:	
Channel thickness:		Channel material:	
Design pressure	Shell: 225 PSI	Operating pressure	Shell: 0 – 200 PSI
	Tubes:		Tubes:
Design Temp.	Shell: 100 Deg F	Operating temperature	Shell: 0 – 250 Deg F
	Tubes:		Tubes:
X-ray: RT 1		Heat treatment: HT	
Code parameters: ASME VIII, Div 1		Coated: No	
Manufacturer: I.P. Constructors		Year built: 1988	
Corrosion allowance: 3.2mm		Manway: Yes	

PRESSURE SAFETY VALVE NAMEPLATE DATA

PSV Tag #	Manufacture	Model #	Serial #	Set Pressure (kPa)	Capacity (scfm)	Service Date
13614F	Mercer	91-27D11V07N1	403597	155 PSI	339	11/2008
CRN #	Service By	Block Valve	Location	Size	Code Stamp	
OG8841.5C	Unified valve	no	top shell	1"x 2"	UV	

SERVICE CONDITIONS-INDICATE ALL THAT APPLY

Sweet	Sour X	Oil	Gas	Water
Amine	LPG	Condensate X	Air	Glycol

Other (Describe):

Inspection Interval _____ **PSV Service Interval** _____

(Determined by MIC in conjunction with Chief Inspector following guidelines of CNRL Owner-User Inspection Program)

Reports reviewed and accepted by:

Mechanical Integrity Coordinator _____ **Date** _____

Fill out all forms as completely as possible. **All information is important!** Use back of sheets to record additional information or sketch if required.
Copy of report to be filed by MIC at site, and copy sent to Chief Inspector

External Inspection Items	G	F	P	N/A	Comments
Insulation Verify sealed around manways, nozzles, no damage present, and there is no egress of moisture.				X	Vessel not insulated.
External Condition Assess paint condition, areas peeling, record any corrosion, damage, etc (record location, size and depth of corrosion or damage)	X				Paint in good overall condition – No exposed metal.
Leakage Record any leakage at flanges, threaded joints, weep holes on repads, etc.	X				No leaks observed.
Saddle/Skirt Assess condition of paint, fire protection, concrete. Look for corrosion, buckling, dents, etc. Look at vessel surface area near supports. Verify no signs of leakage at attachment to vessel and attachment welds are acceptable. Ground wire attached?	X				Saddle: bolted directly to support base. No buckling or dents. No corrosion at attachment welds to vessel. Ground wire attached to saddle.
Anchor Bolts Hammer tap to ensure secure. Look for cracking in treads or signs of deformation.	X				Anchor bolts are securely fastened. No deformation.
Concrete foundation Check for cracks, spalling, etc.				X	
Ladder / Platform Describe general condition, ensure support is secure to vessel, describe any hazards.				X	
Nozzle Assess paint, look for leakage, and ensure stud threads are fully engaged. Record any damage, deflection, etc. Are nozzles gusseted?	X				Stud threads are fully engaged to nuts. No leaks observed. No damage or deflections. Nozzles are not gusseted.
Gauges Ensure gauges are visible, working, no leakage, and suitable for range of MAWP/Temp.	X				Clear and clean – no leakage. Suitable for range of MAWP/Temperature. Temperature gauge 0 – 250 Deg F/pressure gauge 0 – 200 PSI.
External Piping Ensure pipe is well supported. All clamps, supports, shoes, etc. in place. Look for evidence of structural overload, deflection, etc. Paint condition, external corrosion?	X				Piping is well supported – all clamps and supports are in place. No structural overloads or deflections. Paint in good condition – no exposed metal.
Valving Ensure no leaks are visible. Valves are properly supported and chained if necessary.	X				No leaks are visible. Valves are supported properly.
PSV Ensure PSV is set at pressure at or below that of vessel.	X				Location: Top shell - set below MAWP of vessel. Discharge piping is same size as valve outlet. PSV seal in place – no block valve between vessel and PSV.

NDE methods Was UT/ MPI done on vessel (MI coordinator to review results)	X		Ultrasonic corrosion survey carried out – pipe metal thickness detected below nominal minus corrosion allowance. Thickness calculations carried out: 2” Elbow – nominal thickness is 5.5mm / min thickness is 4.8mm / T min thickness is 1.6mm.
Other			

Recommendations or corrective actions : Vessel is Fit for Service or describe corrective actions required)

(MIC to review corrective actions with Operations, discuss with Chief Inspector where necessary, and get remedial action implemented)

Recommendations: No recommendations at this time

Summary: Vessel is in overall good condition, visual external inspection and ultrasonic corrosion survey performed—pipe metal thickness detected below nominal minus corrosion allowance. Thickness calculations carried out to ensure sufficient metal exists for safe operation.


Long term corrosion rate based on greatest thickness loss – no corrosion rate to assess.

Vessel is fit for service.

Inspected By: Andrew Neis / D. Wiedman

Date: April 4, 2012


Photo Table

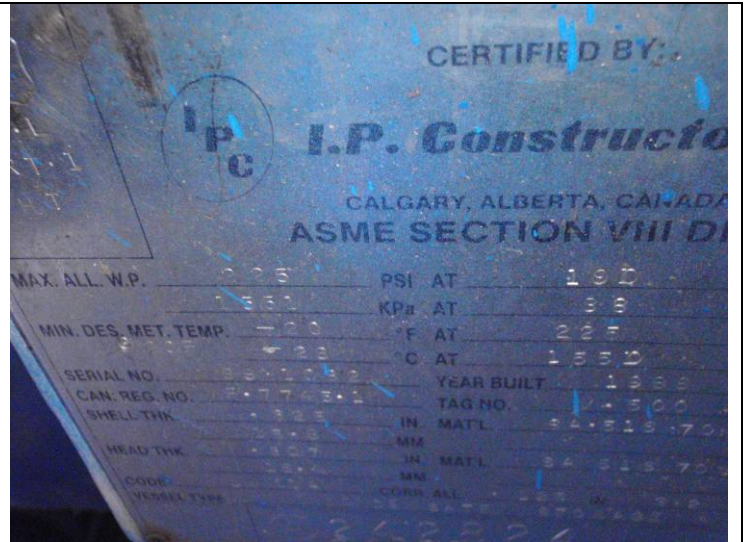

LSD



Vessel data plate

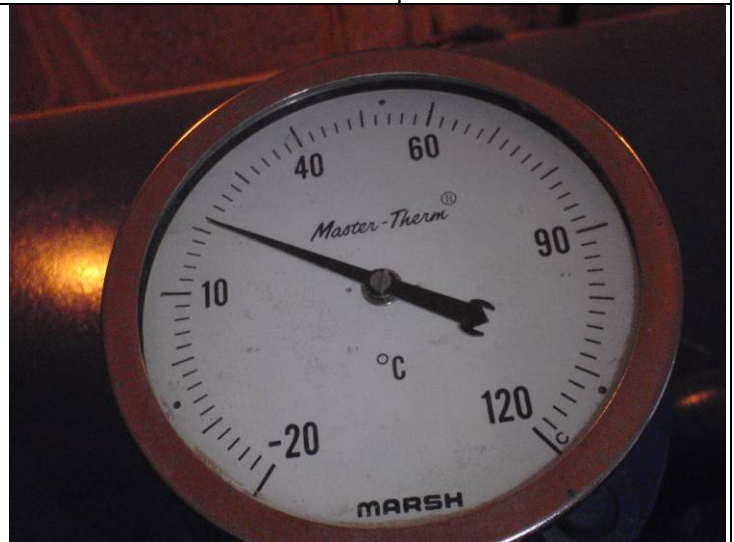


Overview



Temperature gauge



Pressure Gauge

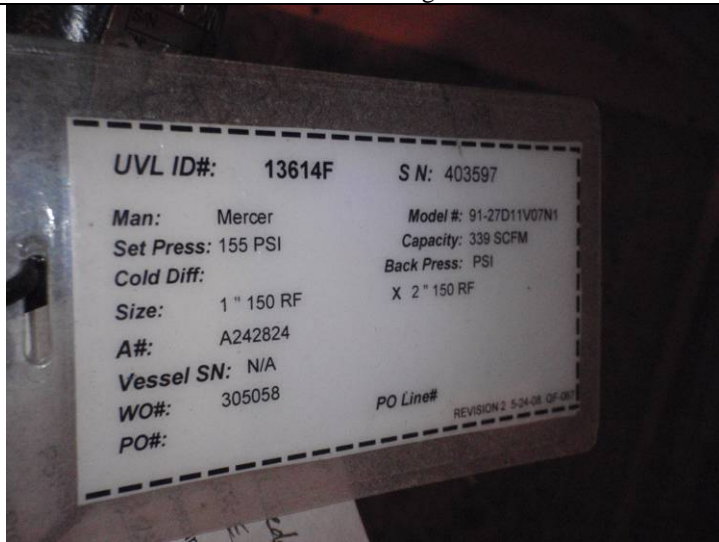

PSV

PSV Service Tag
