

**Canadian Natural Resources Limited
GENERAL PRESSURE VESSEL INFORMATION**

10.111578

District: Fort St. John BC.	Skid No.
Facility: Bucking Horse Compressor Station	Location (LSD): d-44-A/94-G-10
Vessel Name Equipment Number: Glycol Contactor	
Orientation: Vertical	
Status: In Service	Regulatory Inspection

PRESSURE VESSEL NAMEPLATE DATA

"A" or "G" or "S" (Sask.) or BC Registration Number. A 539284		CRN Number: T-3297.21	
Vessel serial number: 2005-7453-06		Size: 12.75 in. x 45ft.	
Shell thickness: 21.4 mm		Shell material: SA106-B	
Head thickness: 17.3 mm		Head material: SA 516-70MT	
Tube wall thickness:		Tube material:	
Tube diameter:		Tube length:	
Channel thickness:		Channel material:	
Design pressure	Shell: 1415 PSI	Operating pressure	Shell: 0 – 1500 PSI
	Tubes:		Tubes:
Design Temp.	Shell: 150 Deg F	Operating temperature	Shell: 0 – 250 Deg F
	Tubes:		Tubes:
X-ray: RT 1		Heat treatment: HT	
Code parameters: ASME VIII, Div 1		Coated: No	
Manufacturer: Alco Gas & Oil		Year built: 2005	
Corrosion allowance: 3.2mm		Manway: No	

PRESSURE SAFETY VALVE NAMEPLATE DATA

PSV Tag #	Manufacture	Model #	Serial #	Set Pressure (kPa)	Capacity (scfm)	Service Date
14566F	Crosby	951102MA	CO235058	1415 PSI	2070	06/2009
CRN #	Service By	Block Valve	Location	Size	Code Stamp	
OG0703.92	Unified valve	no	lower shell	1"x 1"	UV	

SERVICE CONDITIONS-INDICATE ALL THAT APPLY

Sweet	Sour X	Oil	Gas X	Water X
Amine	LPG	Condensate	Air	Glycol X

Other (Describe):

Inspection Interval _____ **PSV Service Interval** _____

(Determined by MIC in conjunction with Chief Inspector following guidelines of CNRL Owner-User Inspection Program)

Reports reviewed and accepted by:

Mechanical Integrity Coordinator _____ **Date** _____


Fill out all forms as completely as possible. All information is important! Use back of sheets to record additional information or sketch if required.
Copy of report to be filed by MIC at site, and copy sent to Chief Inspector

External Inspection Items	G	F	P	N/A	Comments
Insulation Verify sealed around manways, nozzles, no damage present, and there is no egress of moisture.	X				Vessel is partially insulated – no damage visible – no egress of moisture – sealed around nozzles and skid roof
External Condition Assess paint condition, areas peeling, record any corrosion, damage, etc (record location, size and depth of corrosion or damage)	X				Paint in good overall condition – No exposed metal.
Leakage Record any leakage at flanges, threaded joints, weep holes on repads, etc.	X				No leaks observed.
Saddle/Skirt Assess condition of paint, fire protection, concrete. Look for corrosion, buckling, dents, etc. Look at vessel surface area near supports. Verify no signs of leakage at attachment to vessel and attachment welds are acceptable. Ground wire attached?	X				Skirt: bolted directly to skid floor. No buckling or dents. No corrosion at attachment welds to vessel. Ground wire attached to skid.
Anchor Bolts Hammer tap to ensure secure. Look for cracking in treads or signs of deformation.	X				Anchor bolts are securely fastened. No deformation.
Concrete foundation Check for cracks, spalling, etc.				X	
Ladder / Platform Describe general condition, ensure support is secure to vessel, describe any hazards.				X	
Nozzle Assess paint, look for leakage, and ensure stud threads are fully engaged. Record any damage, deflection, etc. Are nozzles gusseted?	X				Stud threads are fully engaged to nuts. No leaks observed. No damage or deflections. Nozzles are not gusseted.
Gauges Ensure gauges are visible, working, no leakage, and suitable for range of MAWP/ Temp.	X				Clear and clean- no leakage. Suitable for range of MAWP / Temperature of vessel. Temperature gauge 0 – 250 Deg F Pressure gauge 0 – 1500 PSI.
External Piping Ensure pipe is well supported. All clamps, supports, shoes, etc. in place. Look for evidence of structural overload, deflection, etc. Paint condition, external corrosion?	X				Piping is well supported – all clamps and supports are in place - No structural overloads or deflections. Paint in good condition – no exposed metal.
Valving Ensure no leaks are visible. Valves are properly supported and chained if necessary.	X				No leaks are visible. Valves are supported properly.
PSV Ensure PSV is set at pressure at or below that of vessel.	X				Location: lower shell - set at MAWP of vessel. Discharge piping is same size as valve outlet. PSV seal in place – no block valve between vessel and PSV.
NDE methods Was UT/ MPI done on vessel (MI coordinator to review results)	X				Ultrasonic thickness survey carried out – no metal thickness detected below nominal minus corrosion allowance.
Other					
<p>Recommendations or corrective actions : Vessel is Fit for Service or describe corrective actions required) (MIC to review corrective actions with Operations, discuss with Chief Inspector where necessary, and get remedial action implemented) Recommendations: No recommendations at this time Summary: Vessel is in overall good condition, visual external inspection and ultrasonic corrosion survey performed—no metal thickness detected below nominal minus corrosion allowance. Short term corrosion rate based on greatest thickness loss (nozzle) 0.067mm per year. Retirement Date to “T”min is year 2132. Vessel is fit for service.</p>					

Photo Table



LSD

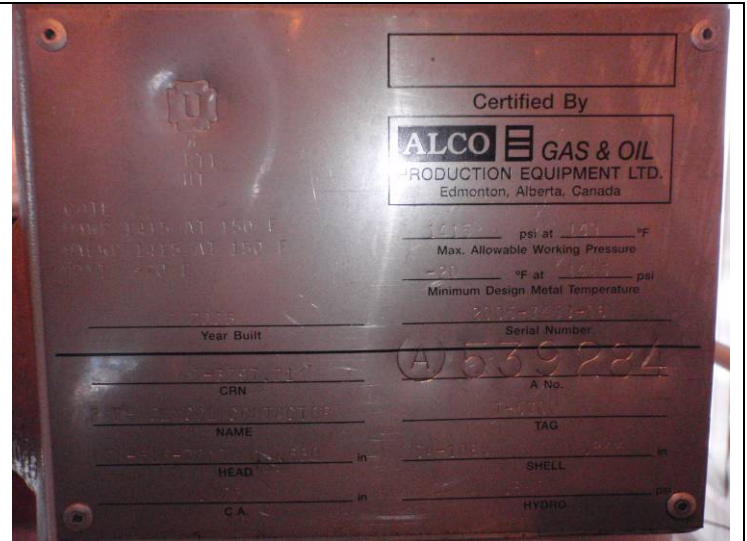

Data plate




Overview



Bolted to skid floor




Overview

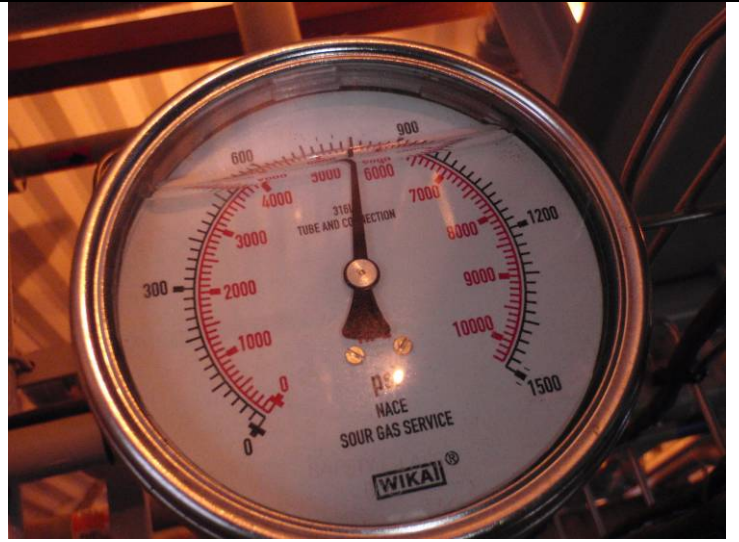

Pressure gauge



PSV

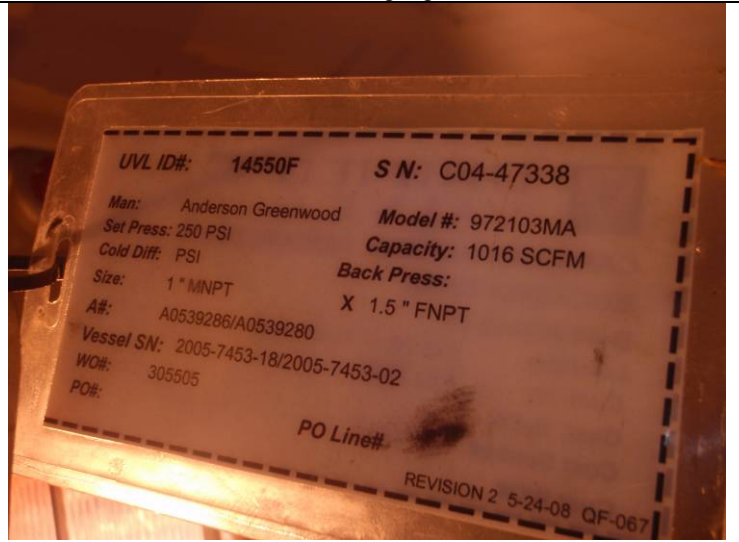

PSV service tag
